5 | 4

Dug 12x15x15' hole in line of E fence did not find C.M.

27-25-6

Sought 5-13-45

32 / 0

Found brick bats 16" deep
½" ø iron rod 36" long at a depth of 16" Lowered set C.M.

Ties from "X" nails

27.1	S.W. from Wood Post
36.5	S.W. from Wood Post
50.9	N.E. from Wood Post
42.2	N.E. from Brace Post
40.9	N. from Corner Post

N

Found 9-26-39

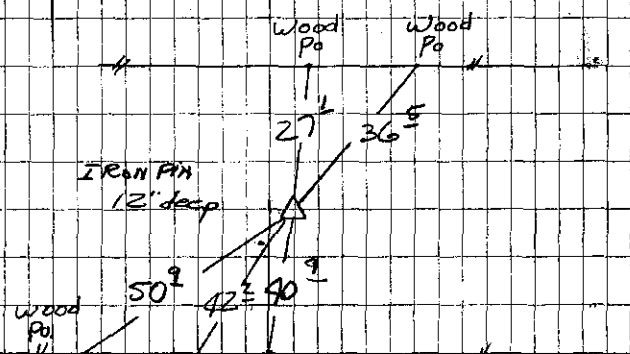

12/10/84 Dug 18 L x 8 W x 3 D hole with backhoe no find.

6-25-96
FOUND 16" Deep
MB

4/3/92 Set ⅝" REBAR from old ties 1½" DEEP remaining evidence C.M. has been excavated out. Kearnes & order of County Engr.
